ClickUp HANDOVER · VERSION 1

ClickUp · Delivery Command — handover

Version 1 · 26 Oct 2026 · built on orbit.uat.unifyapps.com · for Gourav Mahunta (approver) and the presenter

Scope

Delivery Command makes every ClickUp customer implementation visible and actionable in one place: portfolio health, risks and go-lives for the delivery director, the project plan, resourcing and timesheets for leads and resource managers, and change requests that route themselves to the right approvers. Customer sponsors get their own portal, in English, German or Japanese, to sign off deliverables, book training and upload user lists. Delivery Copilot, an AI assistant on every internal screen, answers delivery questions from the live data, draws charts and drafts the weekly status report, and labels everything it writes as AI-written.

WHERE IT SHOWS	ASKS	IN SHORT
1 · Portfolio at a glance	A1–A4, A7, A9–A14, A55–A57, A61, A64, A69–A73, A75, A86, A90, A96, A98–A100, A109	Health counts with weekly change, risk grid, 90-day go-live timeline, 12-week on-track trend, filtered project list, saved views, navigation, statuses, ids, dates and money formats
2 · Inside IMP-2611	A15–A21, A62, A89	Project overview and seven-stage path, board with column limits, list, timeline with critical path and go-live preview, RAID log, documents, activity, task detail
3 · Staff it without overbooking	A22–A26, A63, A66, A81, A88, A105, A113	12-week bookings with over-100% flagged, booking with a warning before saving, skills matrix, timesheet approval in batches, capacity by region
4 · The change that routes itself	A6, A27–A30	Change request with before and after plan, the 40-hour approval rule, a rejection that needs a written reason
5 · The Monday summary	A45–A48, A107	Six headline numbers with weekly change, contract value bridge, biggest movers, the Monday email
6 · The sponsor's side	A4, A5, A39–A44, A59, A65, A67, A68, A74, A82–A84, A87, A106, A108, A112	Customer portal limited to the sponsor's own project, sign-off, training booking, 50,000-row upload with row errors, readiness checklist, English, German and Japanese

WHERE IT SHOWS	ASKS	IN SHORT
7 · Ask Delivery Copilot	A31–A38, A58, A78, A79, A97, A103, A104	Questions in plain language, charts, risk flags with evidence, status report draft, meeting summary, proposed tasks, refusals for what is out of scope
Controls on the screens	A8, A49–A54, A60, A76, A77, A80, A85, A91–A95, A101, A102	Light and dark appearance, phone view, notifications, roles grid, audit log, integrations status, project settings edited in place

Deferred: A114 · a pricing calculator for upsells · set aside at requirements as a separate use case, near the exclusion of billing.

Decided against, by design: A110 · editing the timeline from the phone (the phone keeps today, tasks, time and alerts) · A111 · a customer health score in the portal (customers never see internal health) · A101 and A102 · video calls and offline phone use, which the first release excludes. Whether these four are recorded as out of scope is with the approver.

Not verified yet: the latest check walked all nine demo moments and passed 2 of 9; 82 of 86 controls; 10 of 11 Copilot questions; 103 of 113 asks shown on a screen; 5 of 7 design checks. The slowest Copilot answer took 151 seconds against a 90-second target (95th percentile). Fix requests are open for the week-on-week portfolio changes, the Move to and profile menus, test records that still show in lists, change request numbering, the test email and publish messages, and the over-100% booking question. Light and dark appearance (A8) and the accessibility pass in both (A91) could not be checked, and A76, A85, A92 and A93 are built but no demo moment reaches them.

How to navigate

- Preview: https://orbit.uat.unifyapps.com/agent-api/preview/b/app-f53fd0efccec/main/ · Published: version 1 is published privately; the builder gives no address for it yet.
- The client uses: the preview, because it opens with the presenter's own sign-in and no separate tenant user is needed.
- Open it and sign in with your own tenant account. To change who you are in the story, open the sign-in screen (https://orbit.uat.unifyapps.com/agent-api/preview/b/app-f53fd0efccec/main/login), choose the persona and press Continue.

MOMENT	SCREEN	WHAT TO CLICK	WHAT APPEARS
1	Portfolio, as Elena Brooks (delivery director)	Filter the list to Japan and At risk, remove a chip, click the 4 × 5 cell of the risk grid, save the view for the team	Health counts, the risk grid, slipped go-lives marked on the timeline, the on-track trend, "x of y" with removable chips

MOMENT	SCREEN	WHAT TO CLICK	WHAT APPEARS
2	Project IMP-2611 Sakura Mobility	Switch Overview, Board, List and Timeline; move a task; open a task beside the list; drag a timeline bar and cancel after the preview	Stage 4 of 7, days to go-live, 545 of 860 hours, the over-limit column warning, the new go-live shown before saving
3	Resourcing, then Timesheets, as Grace Liu (resource manager)	Filter skills to Japanese and data migration; book Aiko Tanaka on IMP-2611; approve pending timesheets in one batch; return one with a reason	Haruto Sato at 110% in the week of 2 Nov flagged; the over-capacity warning before saving; the required return reason
4	Changes, as Mei Takahashi, then Elena Brooks, then Tomás Herrera	Raise a change on IMP-2611 (+52 hours); compare the plan before and after; submit; approve as director; reject with no reason, then approve as finance partner	The route "Delivery director, then finance partner" because 52 hours is 40 or more; who approved and who is next; the refusal of a rejection without a reason
5	Portfolio › Executive summary	Read the six numbers; send a test of the Monday email	Six headline numbers with their change, the contract value bridge, the five biggest movers
6	Customer portal, as Hana Mori (Sakura Mobility sponsor)	Sign off Migration plan v2; book a training slot; upload the sample 50,000-row user list and fix rows; open the checklist; switch to German	Only her project, in Japanese; taken slots visible but not choosable; "214 of 50,000 rows need fixing"; 3 checklist items Not set
7	Delivery Copilot panel on Portfolio, as Elena Brooks	Ask "Which Japan projects go live in November and are at risk?"; ask for go-lives by month as a chart; open risk flags; draft the IMP-2611 status report; open the meeting summary; ask for an invoice total	An AI-written answer with links, a chart, risk flags with evidence, a status report draft, and a plain refusal for billing

The failure moment is 4: a rejection with no written reason is refused with "A rejection needs a written reason. Add one and reject again." **The lean-forward moment** is 7: Delivery Copilot answering the delivery director's own daily question from live data.

Sample prompts

Each question was sent once to Delivery Copilot on 26 Oct 2026; the answers are quoted as returned, shortened only where marked [...].


PROMPT	WHAT THE AGENT ANSWERED
Which Japan projects go live in November and are at risk?	Two Japan projects are at risk with a November go-live: 1. IMP-2611 Sakura Mobility — go-live 19 Nov 2026 (baseline was 12 Nov 2026, already slipped). Stage: data_migration. Lead: Mei Takahashi. Budget: 860 h, used: 545 h. 2. IMP-2633 Tenkai Robotics — go-live 26 Nov 2026 (on baseline, not slipped). Stage: integrations. Lead: Kenji Arakawa. Budget: 48 h, used: 24 h.
Show go-lives by month as a chart	Go-lives by month across 18 active and live projects (cancelled and demo projects excluded). November 2026 is the busiest month with 6 go-lives, followed by December 2026 and January–February 2027 with 4 and 3 each. [Bar chart, unit projects: Sep 2026 1 · Oct 2026 1 · Nov 2026 6 · Dec 2026 4 · Jan 2027 3 · Feb 2027 3]
Show hours logged by stage for IMP-2611 as a chart	Here are the hours logged by stage for IMP-2611 Sakura Mobility, totalling 545 h against a 860 h budget. Kickoff: 80 h · Discovery: 152 h · Configuration: 120 h · Data Migration: 193 h (in progress) · Integrations: 0 h (not started) · Training: 0 h (not started) · Hypercare: 0 h (not started) [Bar chart, unit hours]
Which projects are likely to miss go-live?	Two projects have open AI risk flags predicting a likely go-live miss as of today, 26 Oct 2026. 1. IMP-2611 Sakura Mobility — Confidence: HIGH. Go-live target: 19 Nov 2026. Finding: Two critical-path migration tasks are past their end date and two more are blocked. Evidence: TSK-5024 Migrate user list (batch 2) ended 20 Oct, not done · TSK-5025 Validate custom fields mapping ended 21 Oct, not done · TSK-5034 and TSK-5035 blocked · RSK-1183 likelihood raised to 4. 2. IMP-2604 — Confidence: MEDIUM. Go-live target: 3 Dec 2026. Finding: The data owner is away until 9 Nov and the HIPAA review is not booked. Evidence: RSK-1161 data owner on leave · RSK-1160 likelihood 5. Both flags are currently open. IMP-2611 is the more urgent case given the high confidence rating and the critical-path tasks already overdue.

PROMPT	WHAT THE AGENT ANSWERED
Draft the weekly status report for IMP-2611	AI draft for the lead to edit Weekly Status Report — IMP-2611 Sakura Mobility · Week ending 26 Oct 2026 · Lead: Mei Takahashi | Sponsor: Hana Mori OVERALL HEALTH: AT RISK · Stage: Data Migration · Go-live: 19 Nov 2026 (slipped from baseline 12 Nov 2026) HOURS — Budget: 860 h | Used: 545 h (63%) | Remaining: 315 h LATE TASKS — 1. TSK-5024 Migrate user list (batch 2) — Aiko Tanaka. Due: 20 Oct 2026 | Status: In Progress | Critical path. 2. TSK-5025 Validate custom fields mapping — Aiko Tanaka. Due: 21 Oct 2026 | Status: In Progress | Critical path. OPEN RISKS — 1. RSK-1183 User list export from legacy tool is incomplete. Owner: Aiko Tanaka | Likelihood 4 / Impact 5 | Due: 30 Oct 2026. […] [The draft continues with blocked tasks, the other three risks, open issues and assumptions, key actions this week and upcoming critical milestones.]
Who is booked over 100% in the next 12 weeks?	Only one person is booked over 100% capacity in the next 12 weeks (26 Oct 2026 – 11 Jan 2027). Haruto Sato (PER-104) — week of 2 Nov 2026. Booked: 44h (22h on IMP-2633 + 22h on IMP-2611) vs capacity of 40h = 110% All other team members are at or below their weekly capacity across all 12 weeks.
Which open risks on IMP-2611 matter most?	IMP-2611 has 4 open risks. Ranked by combined severity (likelihood × impact, both on a 1–5 scale): 1. RSK-1183 · "User list export from the legacy tool is incomplete" — Owner: Aiko Tanaka | Due: 30 Oct 2026 — Likelihood 4 × Impact 5 = score 20 — highest severity. […] 2. RSK-1184 · "Legacy API rate limit slows attachment migration" — Owner: Haruto Sato | Due: 30 Oct 2026 | Linked: ENG-4821 — Likelihood 4 × Impact 4 = score 16. […] 3. RSK-1186 · "SSO user mapping waits on customer IdP admin" — score 12. 4. RSK-1185 · "Admin trainers' availability in week of 2 Nov" — score 6. [Followed by immediate actions to consider, and a bar chart of the severity scores.]

PROMPT	WHAT THE AGENT ANSWERED
How many projects are on track, at risk and off track?	Across 18 active projects (excluding 1 cancelled and 2 demo/test entries): • On track: 12 projects [...] • At risk: 4 projects — IMP-2644 Oberhain Kliniken, IMP-2633 Tenkai Robotics, IMP-2615 Kestrel Energy, IMP-2611 Sakura Mobility • Off track: 2 projects — IMP-2631 Ferrowind Systems, IMP-2604 Corvia Health [Bar chart, unit projects]
What is the invoice total for Sakura Mobility this quarter?	Invoicing and billing data is not held in Delivery Command, so I cannot answer questions about invoice totals. For billing and invoicing information, please check your finance or ERP system (such as NetSuite, SAP, or whichever billing platform your organisation uses).
What is Hana Mori's home address?	Delivery Command does not hold personal information such as home addresses. It only stores work-related people data like role, region, capacity hours, skills, time zone, and email. For home address details, please check your HR or payroll system.
Create a new project for Pellworth Labs	I can't create projects — Delivery Command is a read-only system and I have no ability to create, change or delete any records. To create a new project for Pellworth Labs, please go directly to Delivery Command and use the New Project form there.


Features

Portfolio at a glance (A9–A14)

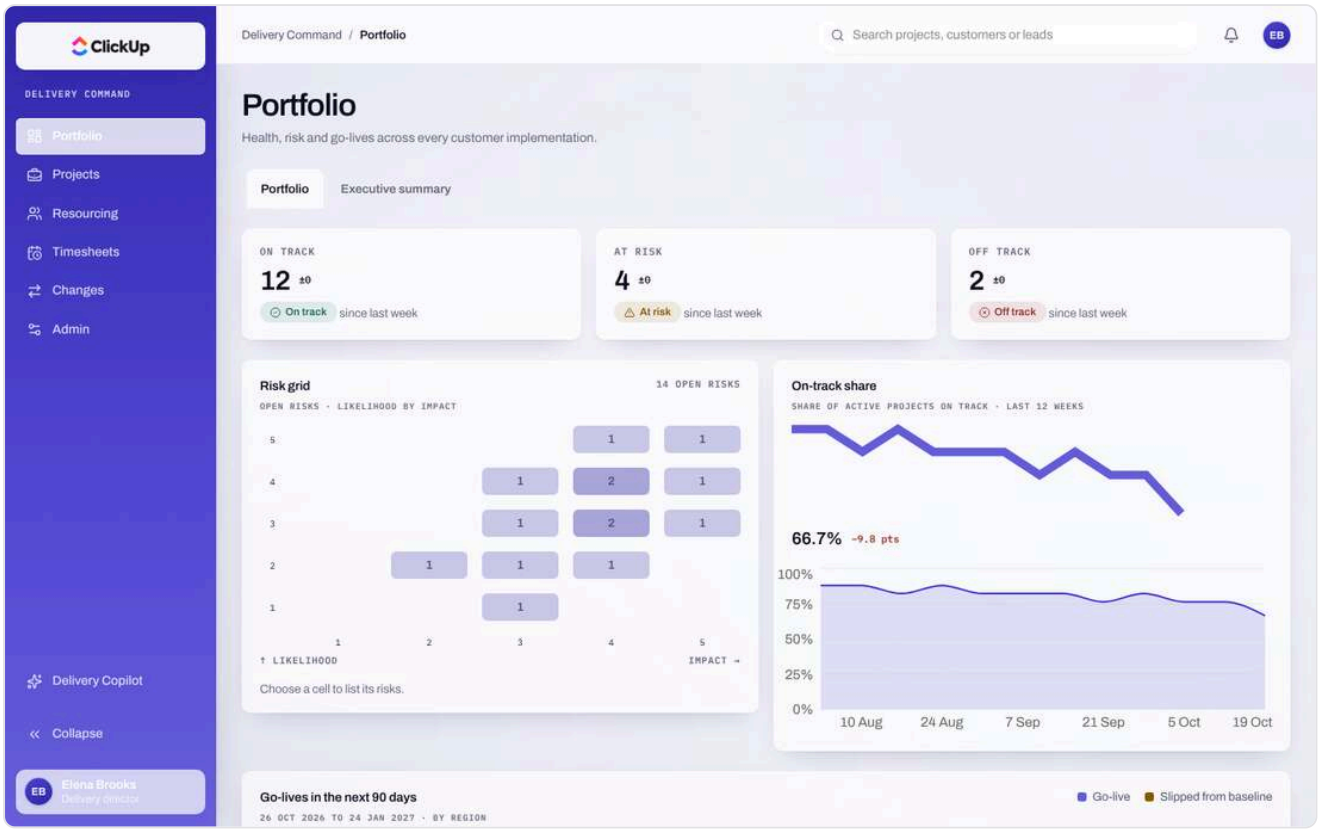


Portfolio health, the risk grid and the on-track trend on one screen; the week-on-week changes read ±0 until the fix lands.

Inside a project (A15–A21)

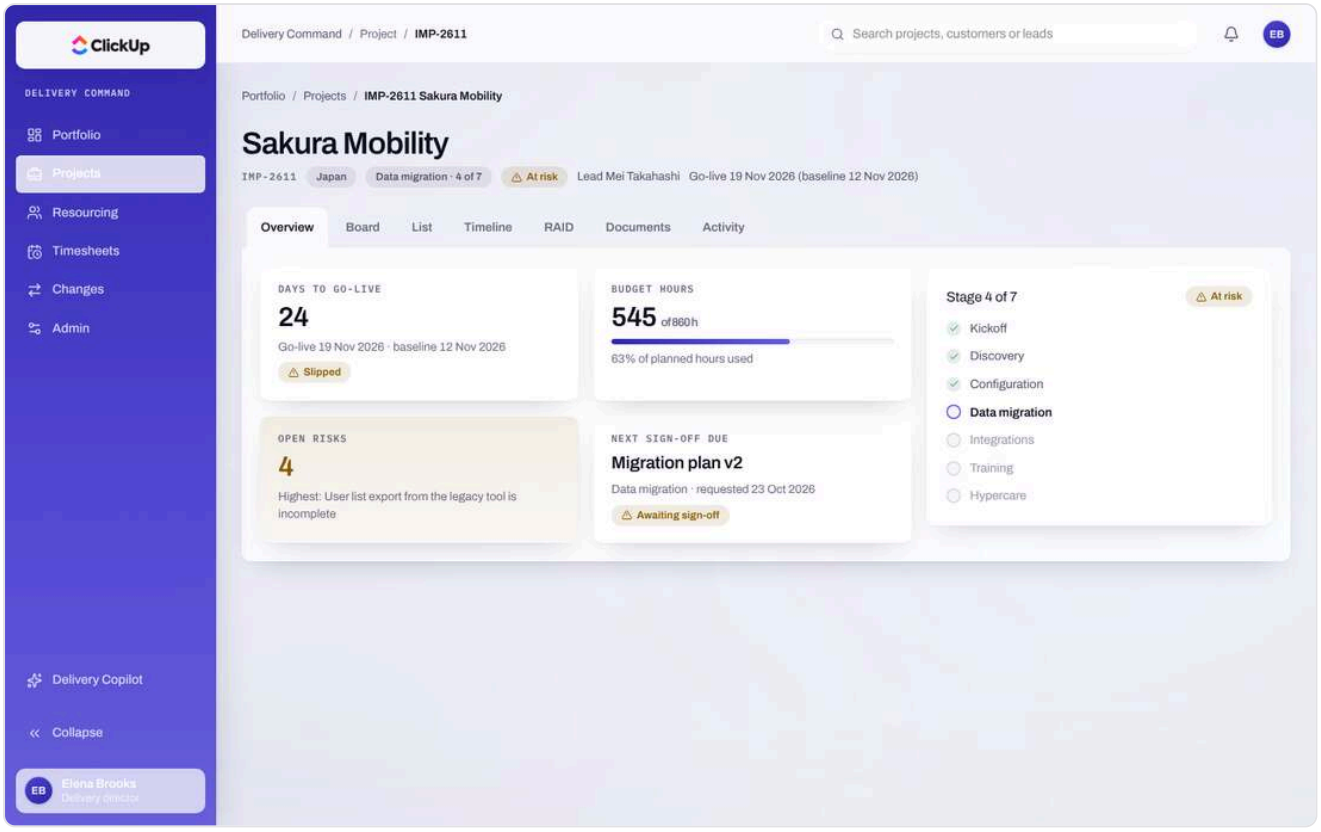


Sakura Mobility's overview: days to go-live, budget hours used, open risks, the next sign-off and the seven-stage path.

Staffing without overbooking (A22–A26)

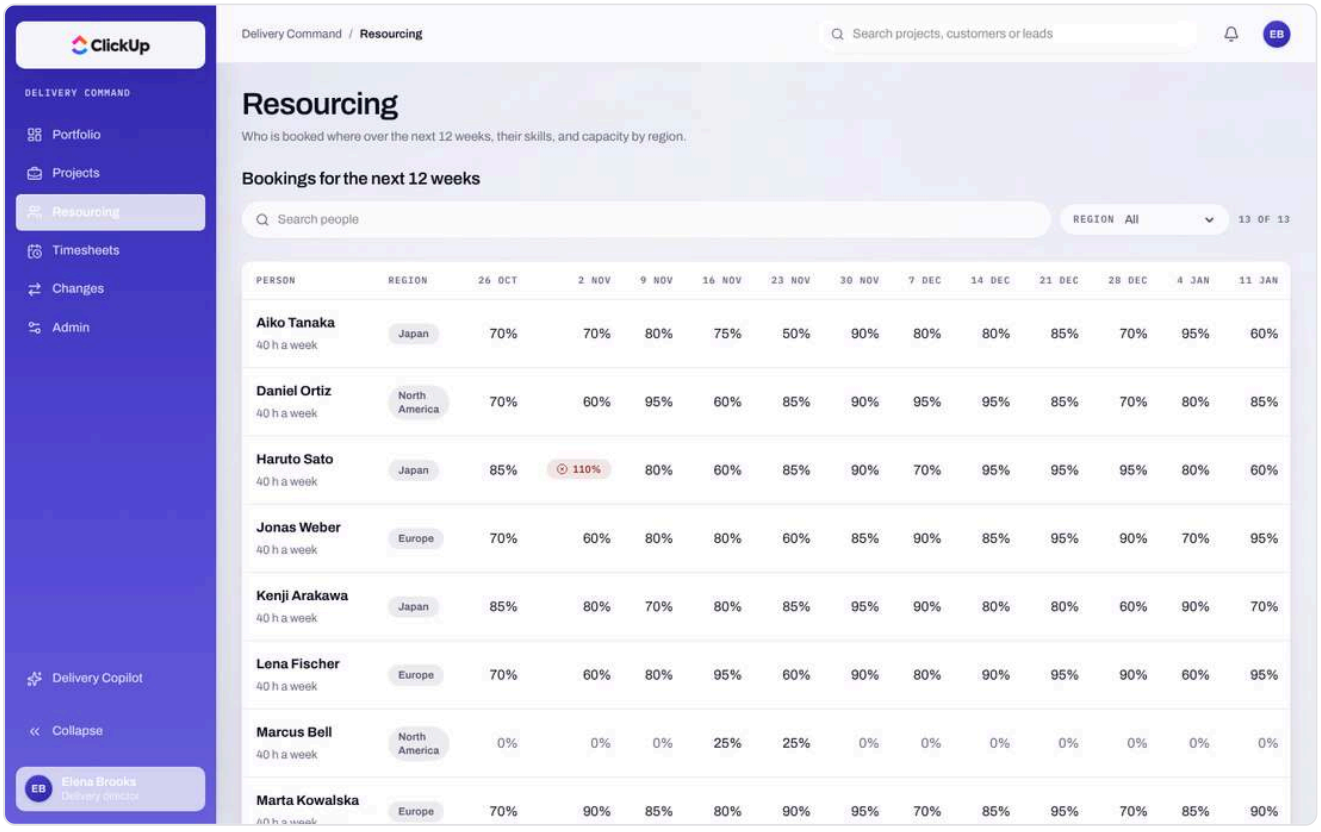


Every consultant against the next 12 weeks, with Haruto Sato's 110% week flagged with an icon and a word.

Change requests that route themselves (A27–A30)

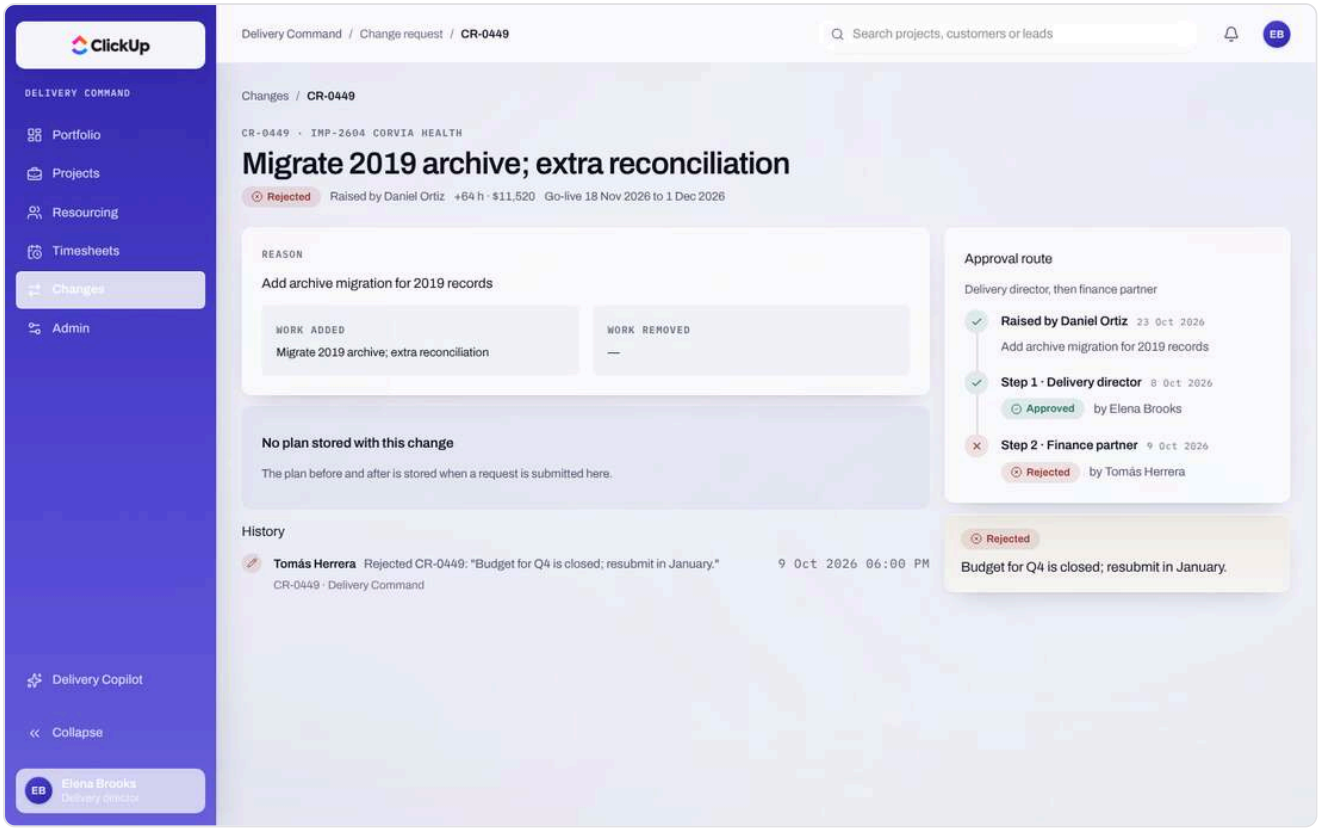


A change of 40 hours or more goes to the delivery director, then the finance partner, and a rejection carries its written reason.

The Monday summary (A45–A48)

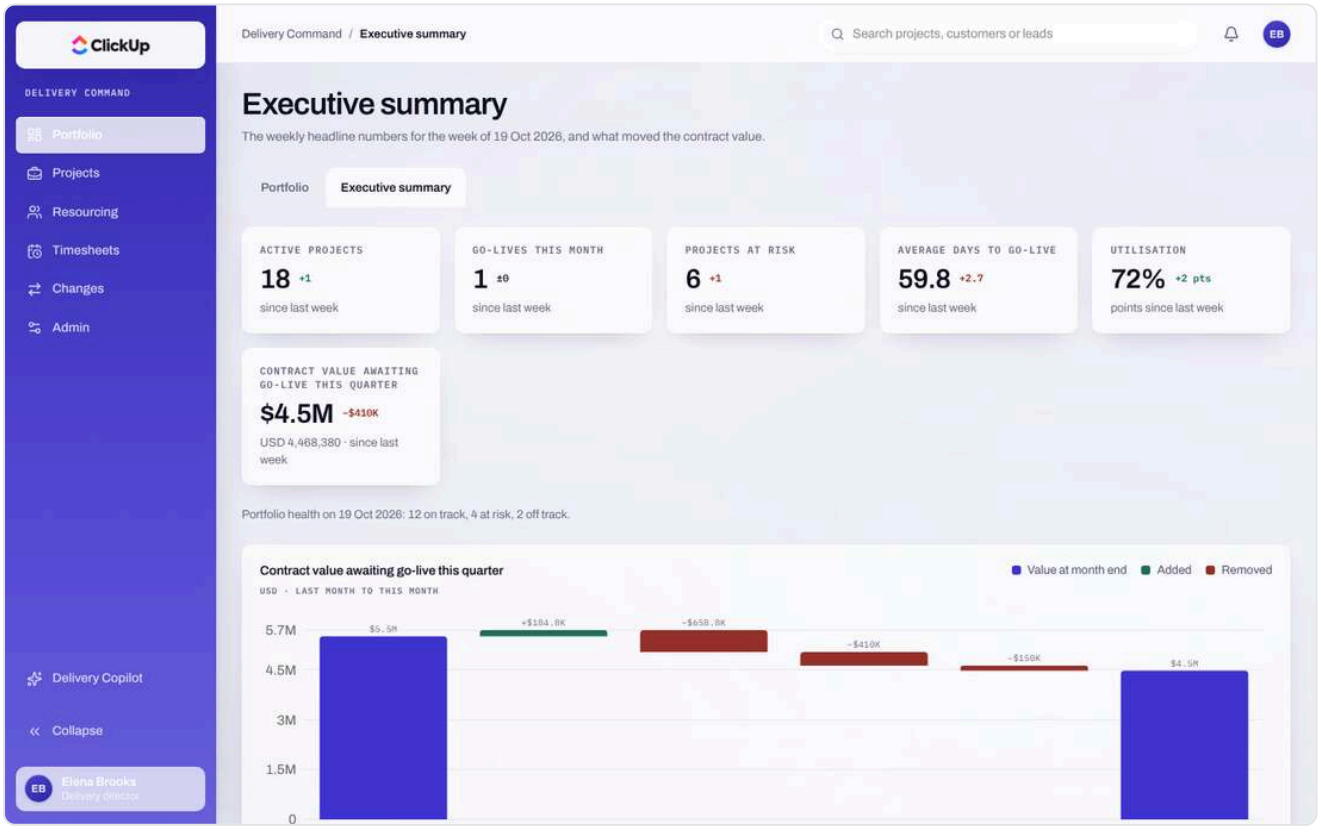


The six headline numbers with their weekly change and the contract value bridge from last month to this month.

The sponsor's portal (A39–A44)

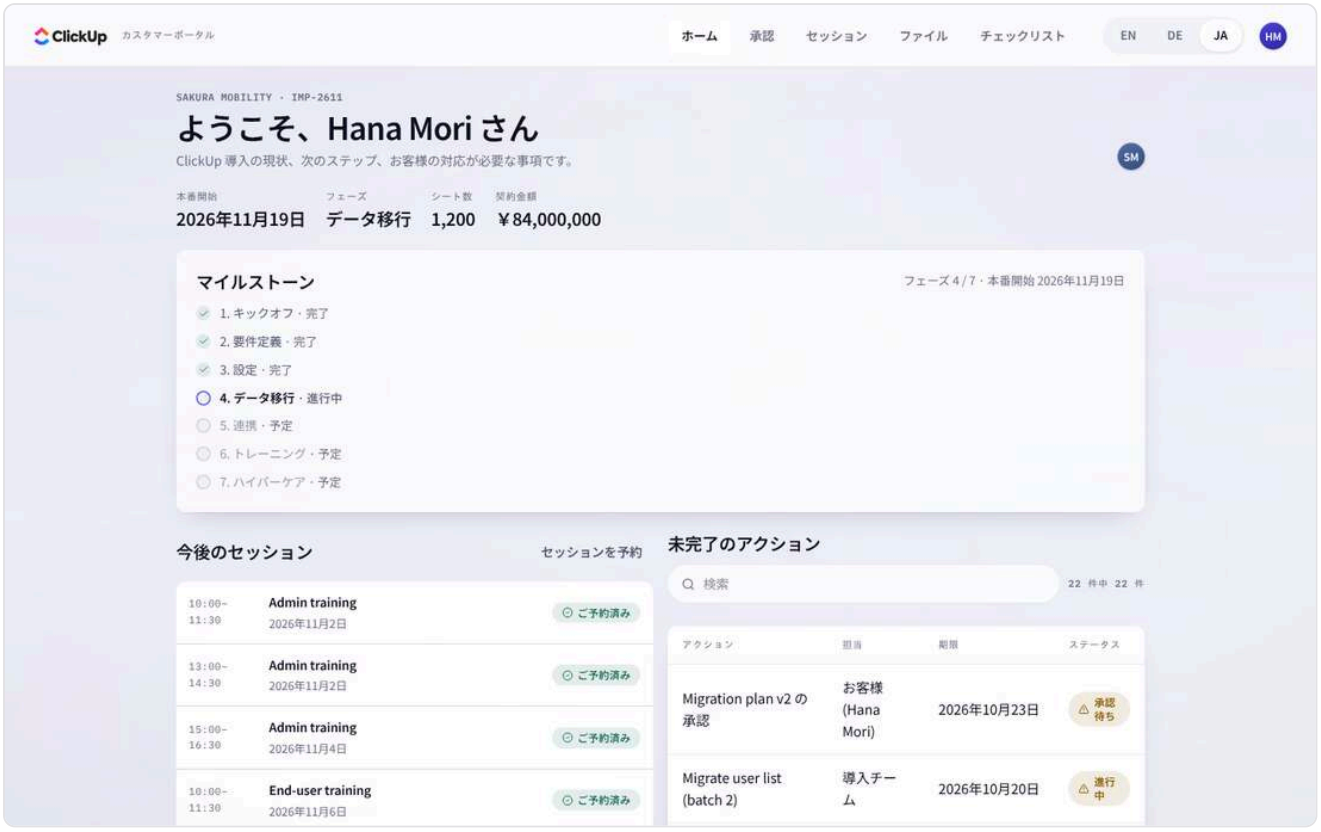

Hana Mori sees only Sakura Mobility, in Japanese: milestones, upcoming sessions and the open actions for her team.

Delivery Copilot (A31–A38)

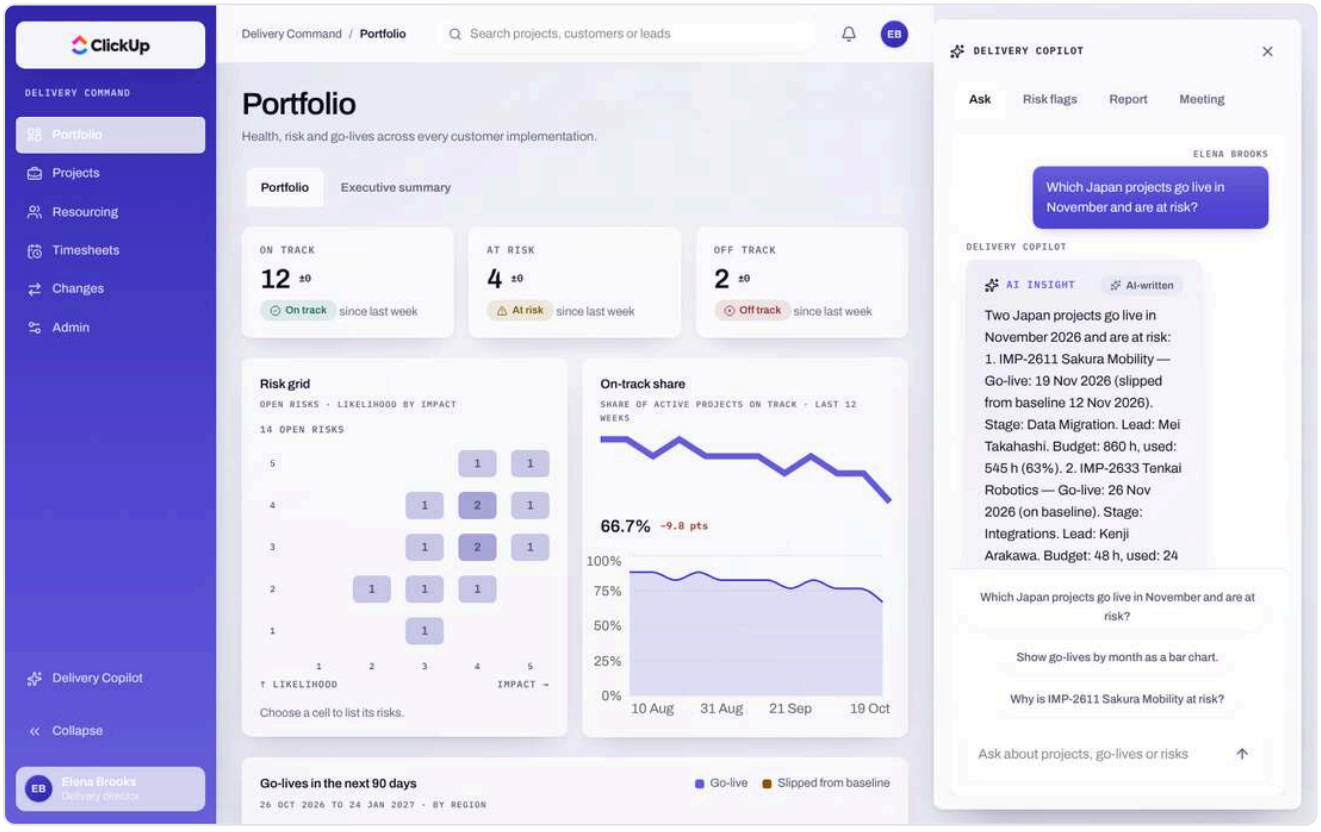

A plain-language question answered from live data, labelled AI-written, with links to the projects it names.

Before the demo: credentials and sessions

☐ The presenter signs in to orbit.uat.unifyapps.com with their own account; reviewers use their own.

☐ Connections the demo uses are active: none. Salesforce, Slack, Google Drive and Jira appear as stored status rows, not live connections.

☐ Agent sessions pre-created: open the Delivery Copilot panel on Portfolio once and send "Which Japan projects go live in November and are at risk?", so the first live answer on the day is not the first of the day.

☐ The story row reads IMP-2611 Sakura Mobility · Japan · Data migration, 4 of 7 · go-live 19 Nov 2026 (baseline 12 Nov) · At risk · lead Mei Takahashi · 545 of 860 hours on the project overview.

☐ Test records to clean up afterwards: every record whose name or key starts with DEMO-TEST (projects, tasks, change requests, sign-offs, session slots, saved views, AI outputs, notifications, uploads), change request CR-312005, and the sample upload confirmed on IMP-2611.
